



Wisconsin Department of Transportation

June 6, 2019

Division of Transportation Systems Development

Bureau of Project Development
4822 Madison Yards Way, 4th Floor South
Madison, WI 53705

Telephone: (608) 266-1631
Facsimile (FAX): (608) 266-8459

NOTICE TO ALL CONTRACTORS:

**Proposal #04: 1080-17-70, WISC 2019 494
Genoa City – Lake Geneva
CTH H Intersection
USH 12
Walworth County**

Letting of June 11, 2019

This is Addendum No. 01, which provides for the following:

Special Provisions:

Revised Special Provisions	
Article No.	Description
3	Prosecution and Progress (Interim Completion Date)

Plan Sheets:

Revised Plan Sheets	
Plan Sheet	Plan Sheet Title (brief description of changes to sheet)
59	Traffic Control Stage 2 – OSOW Signing (revisions to signs located over Illinois state line)

Other

Revise the Contract Time for Completion from a Completion Date of November 27, 2019 to a Completion Date of April 15, 2020.

The responsibility for notifying potential subcontractors and suppliers of these changes remains with the prime contractor.

Sincerely,

Mike Coleman

Proposal Development Specialist
Proposal Management Section

ADDENDUM NO. 01

1080-17-70

June 6, 2019

Special Provisions

3. Prosecution and Progress

*Insert the following section titled **Interim Completion Dates** after the fifth paragraph:*

Interim Completion Dates

Complete all contract work with all lanes of all roadways open to through traffic, except for permanent pavement marking and overhead sign support materials associated with delayed deliveries (poles, arms, and overhead signs), prior to 12:01 AM November 28, 2019. Concrete bases without poles shall be protected by the contractor at their cost.

If the contractor fails to complete all contract work, except for permanent pavement marking and overhead sign support materials associated with delayed deliveries (poles, arms, and overhead signs), and all lanes of all roadways open to through traffic prior to 12:01 AM, November 28, 2019 the department will assess the contractor \$1540 in interim liquidated damages, for each calendar day that the roadways remain closed after 12:01 AM, November 28, 2019. An entire calendar day will be charged for any period of time within a calendar day that the roadways remain closed beyond 12:01 AM.

Complete installation of all permanent pavement marking and overhead sign supports (poles, arms, and overhead signs) prior to 12:01 AM April 16, 2020.


If the contract time expires prior to completing all work specified in the contract, additional liquidated damages will be affixed according to standard spec. 108.11.

Plan Sheets


The following 8½ x 11-inch sheets are attached and made part of the plans for this proposal:

Revised: 59

END OF ADDENDUM

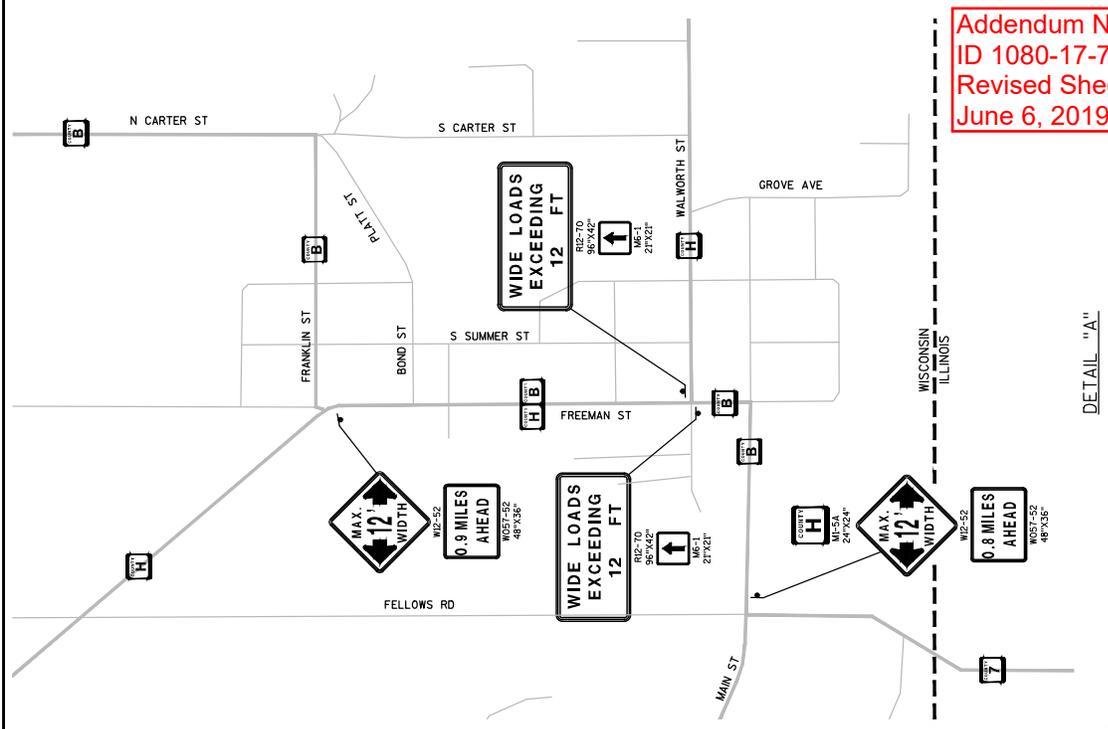

Addendum No. 01
 ID 1080-17-70
 Revised Sheet 59
 June 6, 2019

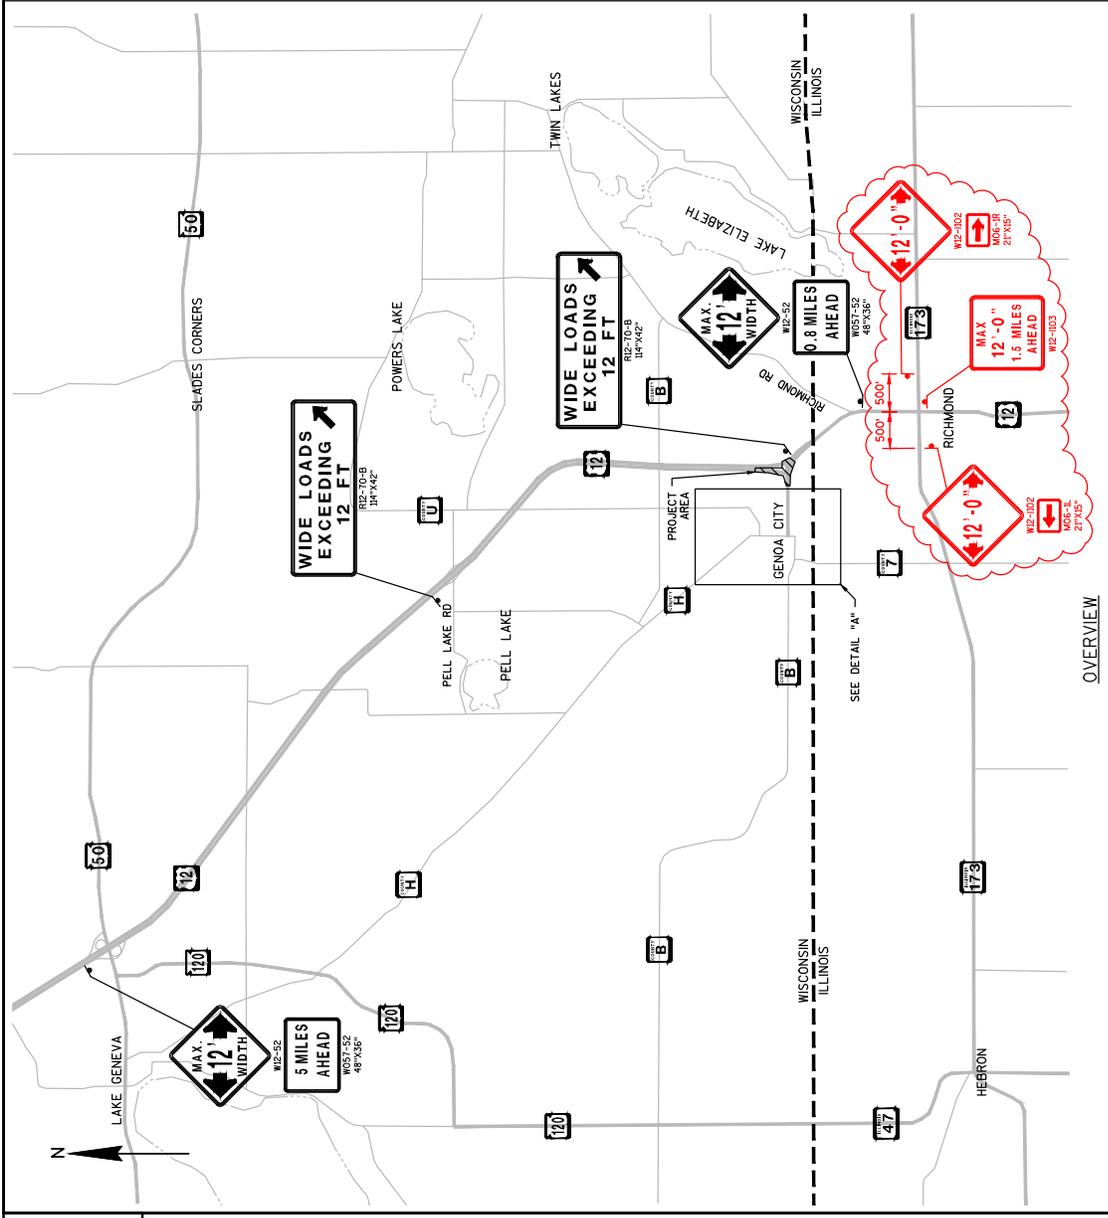

OVERVIEW

DETAIL "A"

OVERSIZE/OVERWEIGHT (OSOW) SIGNING NOTES:
 ALL SIGNING SHOWN ON THIS SHEET SHALL BE INSTALLED PRIOR TO STAGE 2 TRAFFIC SHIFT, AND SHALL BE MAINTAINED THRU THE END OF STAGE 3B.
 ANY DAILY SINGLE LANE CLOSURES REQUIRED AFTER STAGE 3B FOR PUNCH LIST OR MISCELLANEOUS WORK MUST BE SETUP TO PROVIDE 16-FT OF PAVEMENT WIDTH FOR OSOW VEHICLES. IF 16-FT CANNOT BE MAINTAINED, OSOW SIGNING MUST BE PROVIDED PER THIS SHEET.

