Complex Project Schedule Example

	Activity Name	Duration (Weeks)	Start Date	Finish Date
	Programming			
1	Sponsor's Guide Training	6.00	7/19/2024	8/30/2024
2	Certification and Sponsor's Guide Acknowledgement form prepared	4.00	8/30/2024	9/27/2024
3	Certification reviewed and approved	2.00	9/27/2024	10/11/2024
4	State/Municipal Agreement drafted by WisDOT	3.00	6/19/2024	7/10/2024
5	State/Municipal Agreement approved by Sponsor	10.00	7/10/2024	9/18/2024
6	State/Municipal Agreement approved by WisDOT	1.00	10/11/2024	10/18/2024
7	Federal design funding authorization requested and approved	4.00	10/18/2024	11/15/2024
	Consultant Selection and Contracting Services			
8	Consultant solicitation and selection	9.00	11/17/2024	1/19/2025
9	Contract drafted, negotiated and approved	16.00	1/19/2025	5/11/2025
10	Contract approved	3.00	5/11/2025	6/1/2025
11	Notice to proceed issued	1.00	6/6/2025	6/13/2025
	Project Design Delivery			
12	Preliminary design, including surveys, alternatives and environmental studies	15.00	6/20/2025	10/3/2025
	Section 106 reviewed and approved	10.00	10/3/2025	12/12/2025
13	30% plans reviewed	4.00	10/3/2025	10/31/2025
	Environmental Report prepared	4.00	12/27/2025	1/24/2026
14	Environmental Report reviewed and approved	13.00	1/24/2026	4/25/2026
15	60% plans and Design Study Report prepared	2.00	4/25/2026	5/9/2026
16	Plat and documents prepared	6.00	4/25/2026	6/6/2026
17	60% plans reviewed	3.00	5/9/2026	5/30/2026
18	Design Study Report reviewed and approved	4.00	5/9/2026	6/6/2026
19	Final design	56.00	6/13/2026	7/10/2027
20	Plat and documents reviewd and approved	8.00	6/10/2026	8/5/2026
21	Utility plans sent out	4.00	8/5/2026	9/2/2026
22	Real Estate acquisition	48.00	8/5/2026	7/7/2027
23	Utility plans reviewed/updated/approved	9.00	9/2/2026	11/4/2026
24	Utiity relocation	28.00	11/4/2026	5/19/2027
25	PS&E forms prepared	2.00	7/7/2027	7/21/2027
26	PS&E and forms reviewed	2.00	7/21/2027	8/4/2027
27	Federal construction funding authorization requested & approved	4.00	8/11/2027	9/8/2027
28	Request to Advertise approved	1.00	9/8/2027	9/15/2027
29	Lead time to place ads	1.00	9/15/2027	9/22/2027
	Contract Letting			
30	Ad period and bids opened	3.00	9/23/2027	10/14/2027
31	Bids reviewed	1.00	10/14/2027	10/21/2027
32	DBE paperwork submitted by apparent low bidder	1.00	10/21/2027	10/28/2027
33	DBE paperwork reviewed & approved	4.00	10/28/2027	11/25/2027
34	Request to Award reviewed & approved	1.00	11/25/2027	12/2/2027
35	Notice to proceed issued	0.20	12/2/2027	12/3/2027
36	Construction	12.00	3/1/2027	5/24/2027

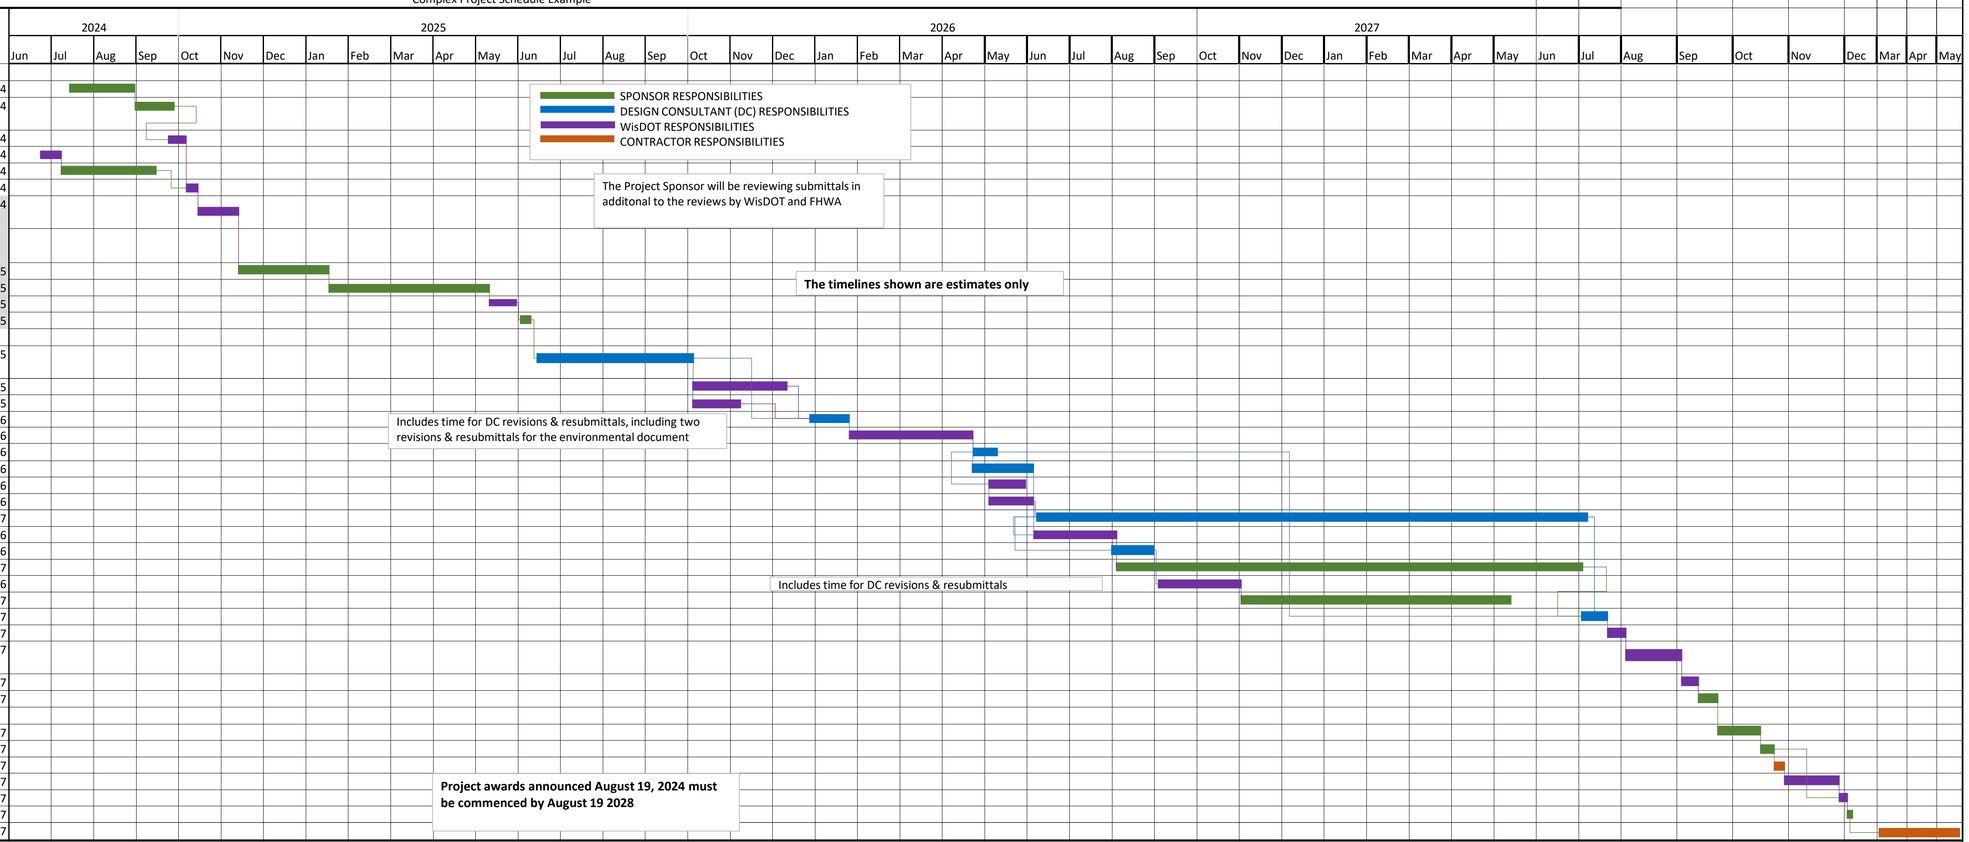

When local funded design is used, these items would not apply/or time frames would be shorter
