




I-94 CONSTRUCTION STAGING TYPICAL SECTION

PROJECT I.D. 1026-00-00 (70)
BLACK RIVER FALLS - TOMAH
COUNTY O TO COUNTY EW (WESTBOUND)
I-94
JACKSON AND MONROE COUNT

AUGUST 2024

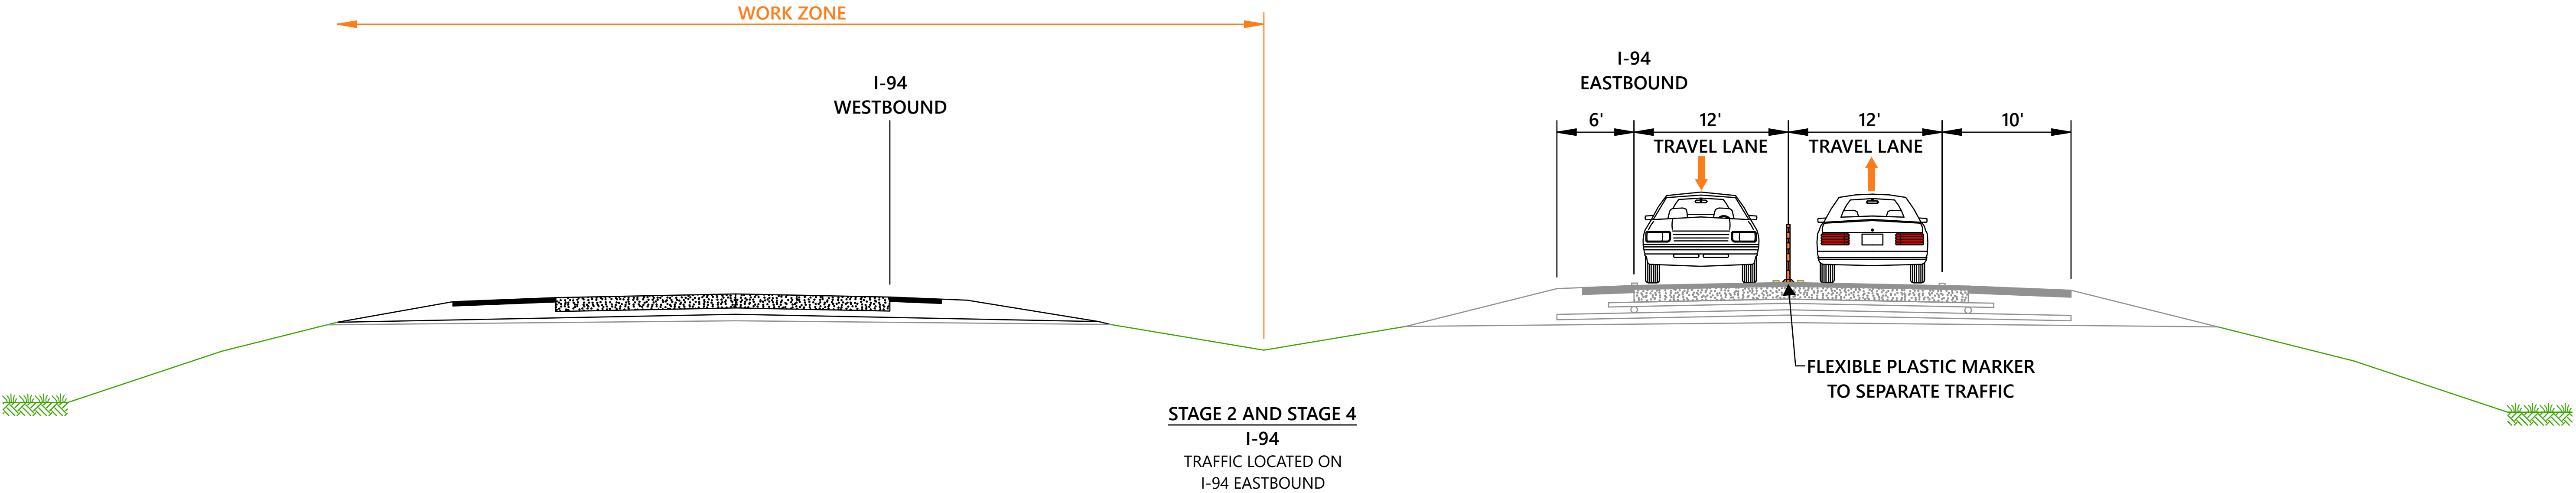

STAGING SUMMARY

2027 CONSTRUCTION

STAGE 1: COMPLETE TEMPORARY WORK ON I-94 UNDER SINGLE LANE CLOSURES

2028 CONSTRUCTION

STAGE 2: CONSTRUCT THE JACKSON COUNTY SEGMENT OF I-94 WESTBOUND WITH BIDIRECTIONAL TRAFFIC ON I-94 EASTBOUND.

STAGE 3:

- COMPLETE TEMPORARY WORK ON I-94 UNDER SINGLE LANE CLOSURES.
- CONSTRUCT I-94 WESTBOUND RAMPS AT COUNTY O AND BETWEEN COUNTY O RAMPS AND MAKE REPAIRS TO THE I-94 BRIDGES OVER COUNTY O.
 - COMPLETE COUNTY O WORK WITH SINGLE LANES CONTROLLED BY TEMPORARY TRAFFIC SIGNALS.
 - SHORT-TERM FULL CLOSURE OF COUNTY O WILL BE ALLOWED IN EACH DIRECTION OF CONCRETE PAVING UNDER I-94.
 - ATV TRAFFIC WILL BE FLAGGED THROUGH THE WORK ZONE AND ACCESS WILL ALWAYS REMAIN FOR ATV TRAFFIC.
 - COUNTY O RAMPS WILL BE CLOSED IN SETS OF TWO RAMPS WITH POSTED DETOURS

2029 CONSTRUCTION

STAGE 4: CONSTRUCT THE MONROE COUNTY SEGMENT OF I-94 WESTBOUND WITH BIDIRECTIONAL TRAFFIC ON I-94 EASTBOUND.

STAGE 5: REMOVE TEMPORARY CROSSOVERS AND GUARDRAIL ON I-94 UNDER SINGLE LANE CLOSURES

2030 CONSTRUCTION

STAGE 6: CONSTRUCT THE I-94 WESTBOUND RAMPS AND COUNTY EW UNDER FULL CLOSURE AND DETOUR.
